

Fort Worth District April COS Project Review Board 3Q10

Bill Workman
COS Manager

Matthew Milliorn
Asst. Program Manager



US Army Corps of Engineers
BUILDING STRONG[®]




Agenda

- SWF Scheduled FY10 CT Actions
- Significant Issues
- Contracting Issues



SWF FY10 CT Actions

- 42 Total FY 10 Contract Actions
 - ▶ Includes 9 awards given back to Geographic Districts

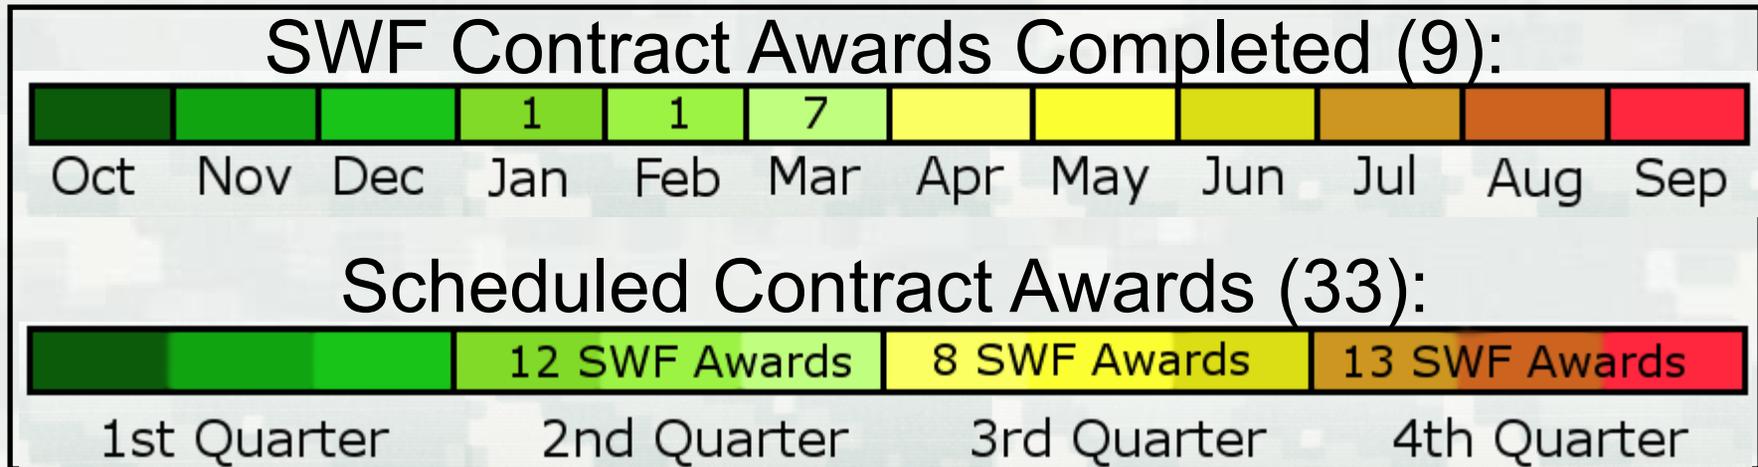

- 4 Slipped Projects:
 - ▶ Fort Knox WT Barracks – PM advised of slip, SSD being reviewed, anticipate award by 16-Apr-10
 - ▶ Fort Carson WT Barracks – PM advised of slip, SSD in Office of Council, anticipate award by 16-Apr-10
 - ▶ Fort Sill UEPH & Fort Sam Houston WT Admin – PMs advised of slip due to BTR requirement, awarding when BTR complete



Significant Issues

- Energy Strategy Meeting (22 Mar)
 - ▶ Huntsville Center visited SWF to discuss partnering opportunities
- Assigned HQUSACE task to investigate standardizing COS products (31-Mar)
- CERL Energy Study (6-7 Apr)
 - ▶ CERL, HQUSACE visited SWF to discuss facility types and energy
 - ▶ SWF Cost Estimating will have active role
- End-State Technical Review
 - ▶ 1st ESTR will be conducted by COS at Ft Campbell 14-15 April
- COSMB 11-13 May in Savannah, GA
- SWD Audit scheduled 25-26 May
- COS/ECSO exploring business collaboration



Contracting Issues

- Regional Contracts
 - ▶ Establishing new MATOCs
 - 1 Contract for StarShip Renovations (Use in OK, GA & SC)
 - 2 Contracts for Warehouses (East & West)
 - ▶ Establishing new MATOCs for existing facility types (6 contracts)
 - 2 NWR Contracts
 - 2 SWR Contracts
 - 2 SER Contracts
 - ▶ Sources Sought were due 9-Apr, reviewing now

