

Fort Worth District May COS Project Review Board 3Q10

Bill Workman
COS Manager

Chevron Blond
Project Coordinator



US Army Corps of Engineers
BUILDING STRONG[®]



Agenda


- SWF Scheduled FY10 CT Actions
- Significant Issues
- Contracting Issues



BUILDING STRONG®

SWF FY10 CT Actions

- 42 Total FY 10 Contract Actions
 - Includes 9 awards given back to Geographic Districts

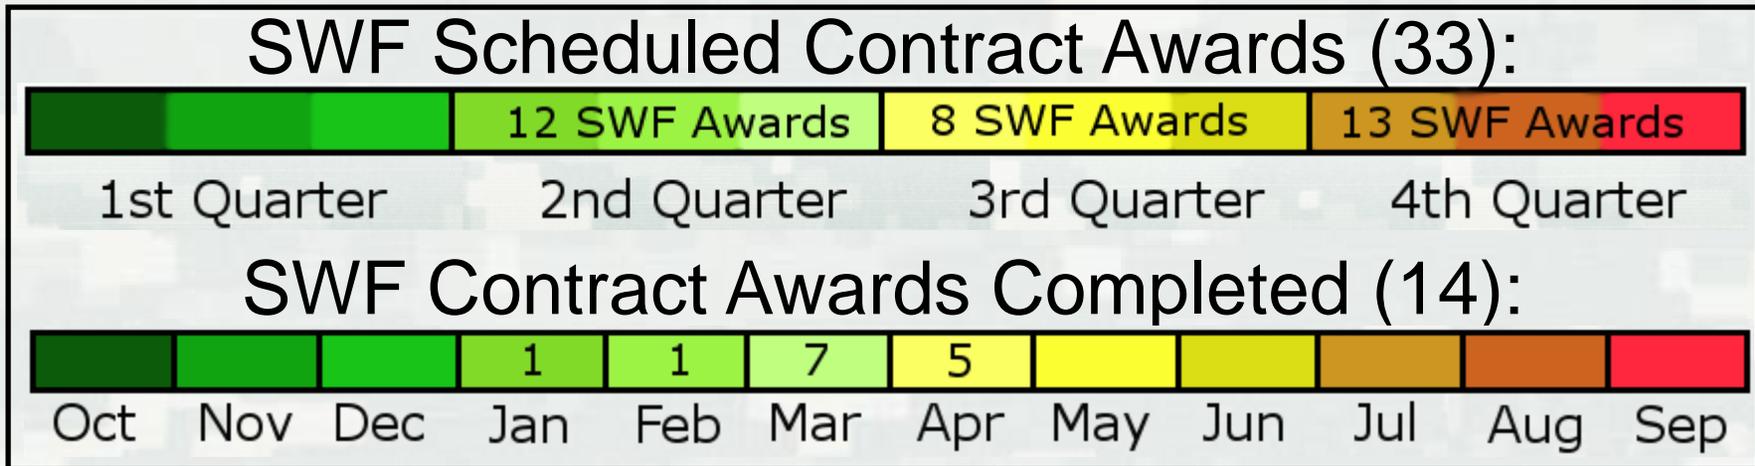

- All Slipped Projects from 2nd Qtr Have Awarded
 - Fort Knox WT Barracks – Awarded 21-Apr-10
 - Fort Carson WT Barracks – Awarded 20-Apr-10
 - Fort Sill UEPH – Awarded 28-Apr-10
 - Fort Sam Houston WT Admin – Awarded 13-Apr-10
- On Schedule for 3rd Qtr Awards



Significant Issues

- COSMB 11-13 May in Savannah, GA
- Briefing initiation of HQUSACE task to investigate standardizing COS products at COSMB
- End-State Technical Review
 - 1st ESTR was successfully conducted by COS at Ft Campbell 14-15 April
 - Next scheduled ESTR is at Ft Leavenworth 3rd Qtr FY 10
- Army Energy Program
 - SWF COS recommended improved indoor solid-state (LED) lighting at Ft Benning
- HQ & SWF Office of Counsel Opinion on FY 11 Ft Drum UEPHs
 - DD1391 scopes for 2 UEPHs cannot be shared
- SWD Audit scheduled 25-26 May
- COS/ECOSO developing business collaboration
 - Meeting 13 May 10 at Ft Bliss with DHS/CBP/OBP Leadership
- Ft Polk requesting deviation to 1+1E UEPH Army Criteria
 - Anticipate requesting to provide 1 room/solider (bedroom, kitchen, bath)



Contracting Issues

- Regional Contracts
 - Establishing new MATOCs
 - 1 Contract for StarShip Renovations (OK, GA & SC)
 - 2 Contracts for Warehouses (East & West)
 - Establishing new MATOCs for existing facility types (6 contracts)
 - 2 NWR Contracts
 - 2 SWR Contracts
 - 2 SER Contracts
 - Developing Acquisition Strategy from Sources Sought Received in April
- Completed approximately half of scheduled awards, realizing an average savings of more than 20%

